



BILL OF MATERIAL						
SHIP MARK	PIECE MARK	QTY	DESCRIPTION	LENGTH	REMARKS	WEIGHT Lbs
2679P1		2	3/8" DIAMOND PL. X 32	4'-10"	A36 ALGRIP SLIP RESISTANT	* 197.4
NOTE: Includes an estimated wt for some items						TOTAL WEIGHT FOR 1 ASSEMBLY 197.4
		MARK	SEQ.	QUANTY	GRID LOCATION	TOP ELEVATION
		2679P1	61	2	E7C11/E8C10	638'-10 3/8"

2679P1
(3/8" DIAMOND PL. X 32 x 4'-10")

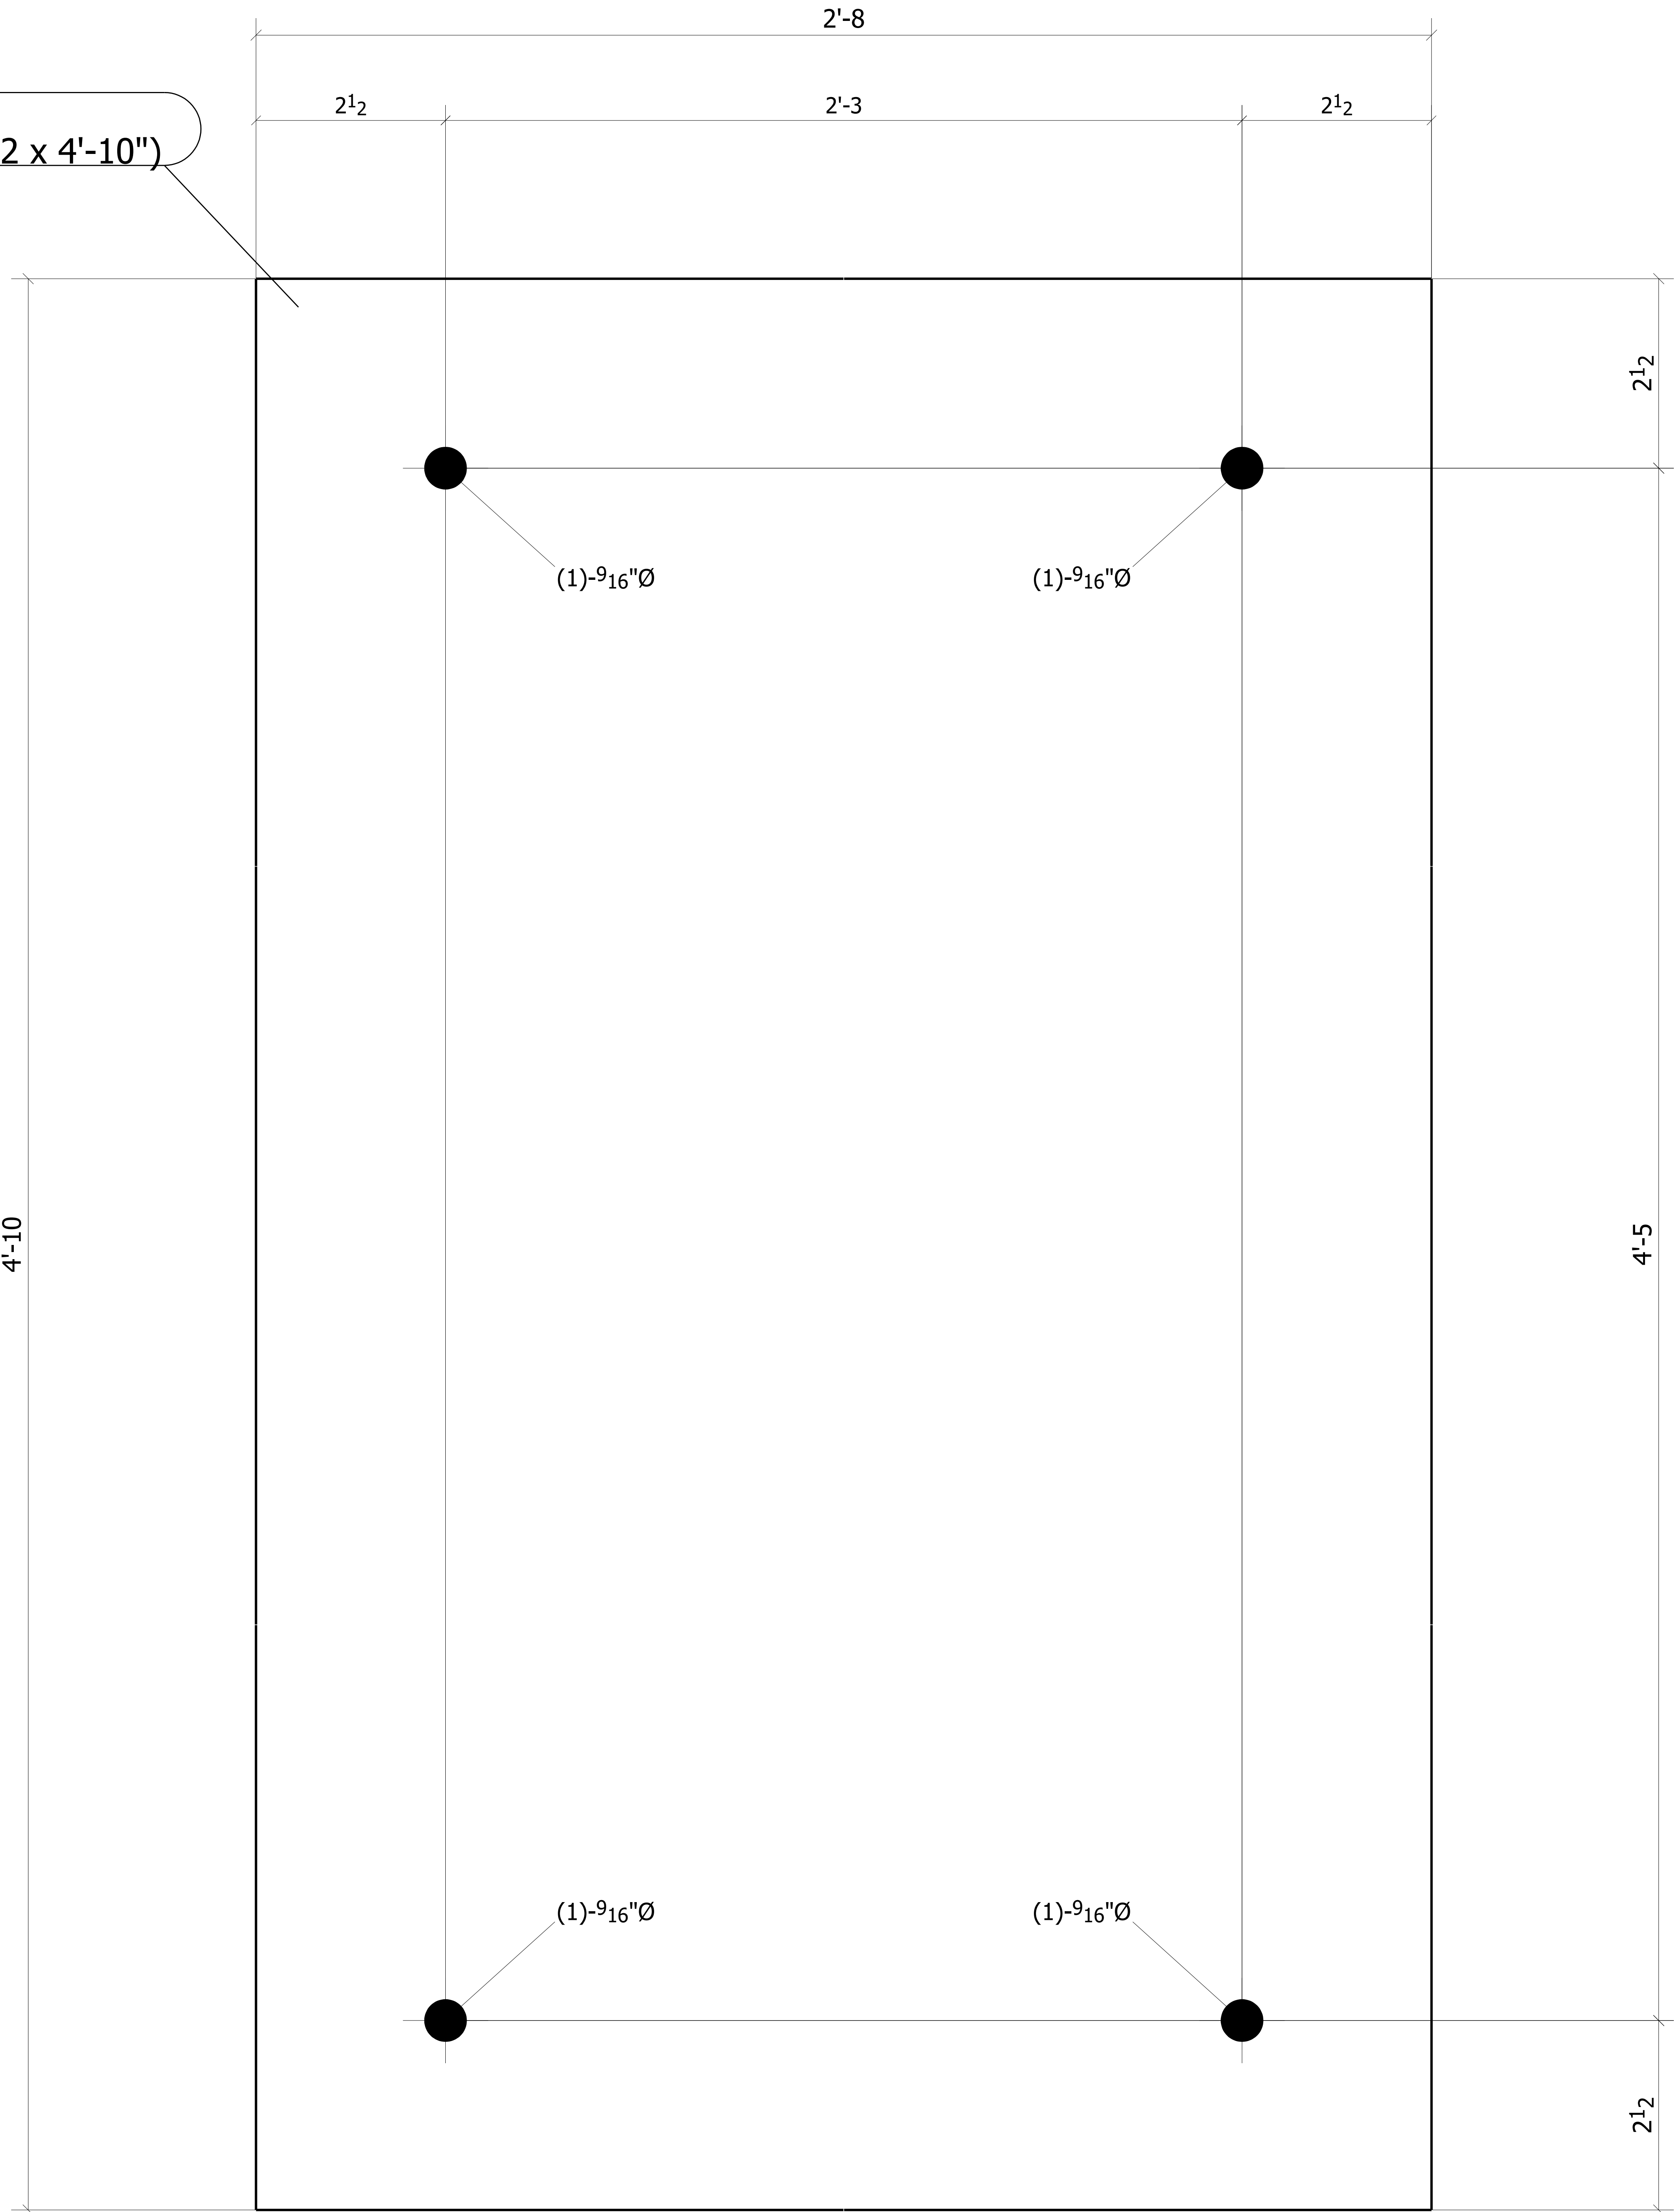

SteelFab of Virginia

5105 Bur Oak Circle, Suite 100
Raleigh, NC 27612
(PO Box 30939 Raleigh, NC 27622-0939)
(Tel.) 919-828-9545
(Fax) 919-828-9720



Job# 27601

REV.	DATE	DESCRIPTION
O	02/12/2020	FOR CONSTRUCTION
A	02/06/2020	FOR APPROVAL

DRAWING NOTES:
FOR PIECE MARKS SEE :
E75

Engineering Design Method: LRFD				
Analysis Type	Left End	Right End	DESCRIPTION	PLATE
AutoCope	N/A	N/A	SURFACE PREP	SSPC-SP3
AutoStandard	N/A	N/A	COATING	1/SC Standard Grey Primer
AutoVerification	N/A	N/A	ARCH.	Perkins + Will
Tekla Ver. 19.1			ENG.	Walter P Moore
			DRAWN BY	SDCo/JOB
			CUSTOMER	Skanska
			CHECKED BY	SDCO/RK

UVA Hospital Expansion
Charlottesville, VA

3/8" DIAMOND PL. X 32 X 4'-10"		Plot Size = 11"x17"	
WELD UNO E70 LH		Plot Date 02/12/20	
SHOP BOLTS UNO 3/4"Ø A325-N-ST		HOLES UNO 13/16"	
DRAWN BY SDCo/JOB		ISSUED 02/12/2020 (REV 0)	
CHECKED BY SDCO/RK		JOB NO. 27601	
		SHT. NO. 2679P1	
